This document is uncontrolled when printed.



BILLY HUGHES BRIDGE – CONSTRUCTION NOISE AND VIBRATION IMPACT STATEMENT ADDENDUM

A2I I Albury to Illabo

CONTRACT NUMBER: 0052

PROJECT DOCUMENT NUMBER:

6-0052-210-EEC-B5-AS-0001_ADD

Docusign Envelope ID: 0D5C3A5C-F29D-47DC-9373-162E67C52770

Document Control

DOCUMENT TITLE:	Billy Hughes Bridge – Construction Noise and Vibration Impact Statement Addendum		
DOCUMENT OWNER:	Chris Standing – Environment, Approvals and Sustainability Manager		
PREPARED BY:	Karen McCann	**TITLE:**	Approvals Advisor
SIGNATURE:	Signed by: E8B888A1E99C4B2...	**DATE:**	23/04/2026
REVIEWED BY:	Clint Dedden	**TITLE:**	Approvals Advisor
SIGNATURE:	Signed by: Clint Dedden 74A1DC2CB083474...	**DATE:**	23/04/2026

Approved by

NAME	TITLE	SIGNATURE	DATE
Chris Standing	Environment, Approvals and Sustainability Manager	DocuSigned by: B00B962219 2149F...	23/04/2026

Revision History

REVISION	REVISION DATE	AMENDMENT	DATE TO CLIENT
A	22/09/2025	For internal review	22/09/2025
0	24/09/2025	For information	24/09/2025
1	09/10/2025	For information	09/10/2025
2	28/10/2025	Updated to include W.004B and W.009B and to include AA comments; issued for information	28/10/2025
3	15/01/2026	Updated to amend W.004B, issued for information	15/01/2026
4	23/02/2026	Updated to consider evening OOHW for W.009B, issued for information	23/02/2026
5	23/04/2026	Updated to consider night OOHW for revised plant list May possession for W.004C, for review	23/04/2026
6	23/04/2026	Updated to consider night OOH for revised plant list May Possession for W.002C, W005A & W.011C For Information	23/04/2026

Disclaimer: This document has been prepared by Martinus. Use of this document shall be subject to the terms of the relevant contract with Martinus. The electronic file of this current revision is the controlled copy. This file is stored on Martinus' server located at Head Office, 3B, 33-35 Belmont Street, Sutherland NSW 2232.

This document is the property of and contains proprietary information owned by Martinus. No permission is granted to publish, reproduce, transmit or disclose to another party, any information contained in this document, in whole or in part, without prior written permission from the issuing authority.

For the purpose of this document, Martinus refers to the Martinus Group of companies.

This document is uncontrolled when printed.

TABLE OF CONTENTS

GLOSSARY **6**

1 INTRODUCTION **8**
1.1 Inland Rail 8
1.2 Purpose of this Addendum 8

2 NOISE ASSESSMENT **14**
2.1 Site establishment activities (W.001B) 14
2.1.1 Scope 14
2.1.2 Assessment 15
2.1.3 Results 15
2.2 Compound operation activities (W.002B) 16
2.2.1 Scope 16
2.2.2 Assessment 16
2.2.3 Results 16
2.3 Compound operation activities (W.002C) 17
2.3.1 Scope 17
2.3.2 Assessment 18
2.3.3 Results 18
2.4 Earthworks (W.004B) 18
2.4.1 Scope 18
2.4.2 Assessment 19
2.4.3 Results 19
2.5 Earthworks (W.004C) 20
2.5.1 Scope 20
2.5.2 Assessment 21
2.5.3 Results 21
2.6 Track Work - Peak (W.005A) 22
2.6.1 Scope 22
2.6.2 Assessment 23
2.6.3 Results 23
2.7 Retaining wall and protection barrier construction (W.009B) 24
2.7.1 Scope 24
2.7.2 Assessment 24
2.7.3 Results 25
2.8 Signalling enabling activities (W.011A) 25
2.8.1 Scope 25
2.8.2 Assessment 26
2.8.3 Results 26
2.9 Installation of signalling infrastructure (W.011B) 26
2.9.1 Scope 26
2.9.2 Assessment 27
2.9.3 Results 27
2.10 Earthworks (W.011C) 28
2.10.1 Scope 28
2.10.2 Assessment 29
2.10.3 Results 29

3 VIBRATION ASSESSMENT **31**
3.1 Site establishment activities (W.001B) 31
3.2 Compound operation activities (W.002B) 31
3.3 Earthworks (W.004B) 31
3.4 Earthworks (W.004C) 31
3.5 Retaining walls and protection barrier construction (W.009B) 31
3.6 Signalling enabling activities (W.011A) 31
3.7 Installation of signalling infrastructure (W.011B) 31

4 CONCLUSION 32
4.1 Mitigation and management measures 32
4.2 Additional mitigation measures 32

APPENDICES 35

APPENDIX A 36
SLR Predict Results (W.001B) Noise 36

APPENDIX B 37
SLR Predict Results (W.002B) Noise 37

APPENDIX C 38
SLR Predict Results (W.002C) Noise 38

APPENDIX D 39
SLR Predict Results (W.004B) Noise and Vibration 39

APPENDIX E 40
SLR Predict Results (W.004C) Noise and Vibration 40

APPENDIX F 41
SLR Predict Results (W.005A) Noise 41

APPENDIX G 42
SLR Predict Results (W.009B) Noise 42

APPENDIX H 43
SLR Predict Results (W.011A) Noise 43

APPENDIX I 44
SLR Predict Results (W.011B) Noise 44

APPENDIX J 45
SLR Predict Results (W.011C) Noise 45

LIST OF TABLES

Table 1: Definitions 6
Table 2: Work scenario description 14
Table 3: Exceedance comparisons for W.001B 15
Table 4: Exceedance comparisons for W.002B 17
Table 5: Exceedance comparisons for W.002C 18
Table 6: Exceedance comparisons for W.004B 20
Table 7: Exceedance comparisons for W.004C 21
Table 8: Exceedance comparisons for W.005A 23
Table 9: Exceedance comparisons for W.009B 25
Table 10: Exceedance comparisons for W.011A 26
Table 11: Exceedance comparisons for W.011B (directional drill) 27
Table 12: Exceedance comparisons for W.011B (vacuum truck) 28
Table 13: Exceedance comparisons for W.011C 29

LIST OF FIGURES

Figure 1: PROJECT ENHANCEMENT SITES 8
Figure 2: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.001B AND W.004B) 10
Figure 3: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.002B) 11
Figure 4: CNVIS WORK AREA REQUIRED FOR BILLY HUGHES WITH UPDATED LIST OF EQUIPMENT (W.009B) 12
Figure 5: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.011A) 13
Figure 6: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.011B) 13

Figure 7: ADDITIONAL MITIGATION MEASURES MATRIX - NOISE.....33
Figure 8: ADDITIONAL MITIGATION MEASURES MATRIX - VIBRATION 34
Figure 9: ADDITIONAL MITIGATION MEASURES MATRIX - NOTES 34

GLOSSARY

Specific terms and acronyms used throughout this plan are listed and described in Table 1 below.

TABLE 1: DEFINITIONS

TERM	DEFINITION
A2I	Albury to Illabo Project approved under Section 5.19 of the EP&A Act on 8 October 2024 and modified on 13 August 2025
Addendum	Addendum to the endorsed Construction Noise and Vibration Impact Statement
CA	Consistency Assessment
CoA	Conditions of Approval for SSI-10055
CNVIS	Construction Noise and Vibration Impact Statement
km	Kilometres
m	Metres
NML	Noise Management Levels
OOH	Out-of-hours
Project	Albury to Illabo Project approved under Section 5.19 of the EP&A Act on 8 October 2024
RBL	Rating Background Level
SLR Predict	SLR Predict, the A2I noise and vibration management tool
SSI	State Significant Infrastructure
T	Tonnes
W.001	Work Scenario 1
W.001B	Work Scenario 1B
W.002	Work Scenario 2
W.002B	Work Scenario 2B
W.002C	Work Scenario 2C
W.004B	Work Scenario 4B
W.004C	Work Scenario 4C
W.005A	Work Scenario 5A
W.009B	Work Scenario 9B
W.011A	Work Scenario 11A

TERM	DEFINITION
W.011B	Work Scenario 11B
W011C	Work Scenario 11C

1 INTRODUCTION

1.1 Inland Rail

Inland Rail is an approximate 1,600 kilometres (km) freight rail network that will connect Beveridge and Kagaru via regional Victoria, New South Wales and Queensland. The Inland Rail route would involve using approximately 1,000 km of existing track (with enhancements and upgrades where necessary) and 600 km of new track, passing through 30 local government areas. Inland Rail will accommodate double-stacked freight trains up to 1,800 metres (m) long and 6.5 m high.

The Albury to Illabo (A2I) section (the Project) forms a key component of the Inland Rail program.It is a 185 km section of existing rail corridor located in regional NSW between the towns of Albury and Illabo. Works would include track realignment, lowering and/or modification within the existing rail corridor, modification, removal or replacement of bridge structures (rail, road and/or pedestrian bridges), raising or replacing signal gantries, level-crossing modifications and other associated works.

Precinct	Enhancement sites
Albury Precinct	Murray River bridge
	Albury Station pedestrian bridge
	Albury Yard clearances
	Riverina Highway bridge
	Billy Hughes bridge
	Table Top Yard clearances
Greater Hume-Lockhart	Culcairn pedestrian bridge
	Culcairn Yard clearances
	Henty Yard clearances
	Yerong Creek Yard clearances
	The Rock Yard clearances
Wagga Wagga	Uranquinty Yard clearances
	Pearson Street bridge
	Cassidy Parade pedestrian bridge
	Edmonson Street bridge
	Wagga Wagga Station pedestrian bridge
	Wagga Wagga Yard clearances
	Bomen Yard clearances
Junee	Harefield Yard clearances
	Kemp Street bridge
	Junee Station pedestrian bridge
	Junee Yard clearances
	Olympic Highway underbridge
	Junee to Illabo clearances



FIGURE 1: PROJECT ENHANCEMENT SITES

1.2 Purpose of this Addendum

This Construction Noise and Vibration Impact Statement Addendum (Addendum) has been prepared to identify and assess revised plant and equipment required to support and enable works taking place outside standard construction hours during the ARTC May possession window commencing Friday 1st May to Tuesday 5th May associated with the Billy Hughes Bridge enhancement site (Billy Hughes). Specifically, this Addendum considers the scenarios (W.002C), (W.005A), and (W.011C) being carried out during the night OOH period, and with a revised plant list from previous versions of the above scenarios and the endorsed Billy Hughes Bridge CNVIS. This Addendum will form part of the endorsed Construction Noise and Vibration Impact Statement (CNVIS) (Doc No: 6-0052-210-EEC-B5-AS-0001) for Billy Hughes. This Addendum should be reviewed in conjunction with the CNVIS for Billy Hughes, including adopted Rating Background Levels (RBL), Noise Management Levels (NML) and assessment criteria in accordance with the Conditions of Approval (CoA) (SSI-10055).

The following scenarios are considered in previous CNVIS Addendums:

- W.001B – revised work area (Figure 2) for the site establishment work scenario (W.001);
- W.002B – revised work area (Figure 3) for compound operation scenario (W.002);
- W.004B – revised work area (Figure 2) for the earthworks scenario (W.004);
- W.009B – revised equipment list and construction hours for the retaining wall and protection barrier construction scenario (W.009) in the work area (Figure 4) assessed in the endorsed CNVIS;
- W.011A – revised work area (Figure 5) for signalling enabling works scenario;
- W.011B – revised work area (Figure 6) for installation of signalling infrastructure:
- W.004C – revised plant and equipment list for the earthworks scenario (W.004).

The following scenarios are considered in this CNVIS Addendum:

- W.002B – revised plant and equipment list for compound operation scenario (W.002);
- W.005A – revised plant and equipment list for Track Work Peak scenario (W.005);
- W.011C – revised plant and equipment list for the signalling work scenario (W.011).



FIGURE 2: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.001B AND W.004B)



FIGURE 3: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.002B)



FIGURE 4: CNVIS WORK AREA REQUIRED FOR BILLY HUGHES WITH UPDATED LIST OF EQUIPMENT (W.009B)



FIGURE 5: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.011A)



FIGURE 6: REVISED WORK AREA REQUIRED FOR BILLY HUGHES (W.011B)

2 NOISE ASSESSMENT

The potential construction noise levels from the proposed works have been predicted using SLR Predict, the A2I project-specific noise and vibration tool. This CNVIS Addendum assesses the work scenarios identified in Table 2.

TABLE 2: WORK SCENARIO DESCRIPTION

ID	Scenario	Description	Total Lw
W.001B	Site establishment	Site compound delivery and set up, access Road and laydown construction	114
W.002B	Compound operation	Operation of the site compound and delivery of materials / equipment	114
W.002C	Compound operation	LV / HV designated parking Emergency assembly point	
W.004B	Earthworks	Earthworks / Bulk excavation Stockpiling	116
W.004C	Earthworks	Earthworks / Bulk excavation Stockpiling	122
W.005A	Track work - Peak	Track work	
W.009B	Retaining wall and protection barrier construction	Deflection wall construction Soil nail wall construction	119
W.011A	Signalling work – signalling enabling activities	Access for cable pulling and testing works	106
W.011B	Signalling work – installation of signalling infrastructure	Installation of signalling infrastructure	101
W.011C	Signalling Work	Disconnecting and reconnecting of signalling cables Testing of signalling functions post relocation	

2.1 Site establishment activities (W.001B)

2.1.1 Scope

The revised work area (Figure 2) consists of the work area identified in the endorsed CNVIS, additional area considered as part of the approved Project and additional work area identified in the Billy Hughes Bridge Consistency Assessment (CA) (Doc No: 6-0052-210-EAP-B5-AS-0001) following further construction planning.

Methodology

- Site compound delivery and set up
- Haul road and laydown construction

Plant and equipment

- Articulated dump truck
- Crane – mobile
- Elevated work platform

- Excavator – slasher
- Front end loader
- Generator
- Hand tools (electric)
- Hand tools (power)
- Light vehicle
- Roller – non-vibratory
- Tractor – slasher
- Truck – medium rigid (20T)
- Truck – truck & dog
- Watercart

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday
- Daytime out-of-hours (OOH)
  - 8am to 6pm Sunday and Public Holidays

2.1.2 Assessment

The revised work area has been assessed utilising SLR Predict. The highest noise generating items of plant and equipment in this work scenario (front end loader and articulated dump truck) have been considered as a worst-case scenario, with 100% utilisation within a 15-minute assessment period.

2.1.3 Results

The SLR Predict results are presented in Appendix A, for daytime out of hours, as the most affected period (site establishment will not be undertaken during evening or night out of hours). Table 3 provides a summary of the exceedances identified through various assessments. It compares the following:

- W.001 exceedances identified in the Billy Hughes CNVIS
- W.001B exceedances identified in the SLR Predict results for the revised work area shown in Figure 2.

TABLE 3: EXCEEDANCE COMPARISONS FOR W.001B

ASSESSMENT RESULTS (DAY OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.001 CNVIS	W.001B SLR Predict – revised work area
Total Lw (dBA)	115	114
Noticeable (1-5 dB)	0	1
Clearly Audible (6-15 dB)	0	1
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 3 shows that there are minimal changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.001B.

2.2 Compound operation activities (W.002B)

2.2.1 Scope

The revised work area (Figure 3) consists of the work area identified in the endorsed CNVIS and additional compound area considered as part of the approved Project.

Methodology

- Operation of site compound
- Delivery of materials/equipment

Plant and equipment

- Centrifugal fan
- Compressor
- Crane franna (20t)
- Front end loader
- Generator
- Hand tools (electric)
- Light vehicles
- Truck – medium rigid (20t)
- Truck – truck & dog
- Watercart

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime OOH:
  - 8am to 6pm Sunday and Public Holidays
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.2.2 Assessment

The revised work area has been assessed utilising SLR Predict. The highest noise generating items of plant and equipment in this work scenario (front end loader and compressor) have been considered as a worst-case scenario, with 100% utilisation within a 15-minute assessment period.

2.2.3 Results

The SLR Predict results are presented in Appendix B, for nighttime out of hours, as the most affected period. Table 4 provides a summary of the exceedances identified through various assessments. It compares the following:

- W.002 exceedances identified in the Billy Hughes CNVIS
- W.002B exceedances identified in the SLR Predict results for the revised work area shown in Figure 4.

TABLE 4: EXCEEDANCE COMPARISONS FOR W.002B

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.002 CNVIS	W.002B SLR Predict – revised work area
Total Lw (dBA)	113	114
Noticeable (1-5 dB)	0	1
Clearly Audible (6-15 dB)	0	1
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 4 shows that there are minimal changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.002B.

2.3 Compound operation activities (W.002C)

2.3.1 Scope

The following plant and equipment list has been collated for Billy Hughes Bridge during the ARTC May Possession 2026, commencing Friday 1st May to Tuesday 5th May. Works taking place outside standard construction hours, as defined under section L4.1 of the EPL (# 21984), have therefore been assessed for noise impact and appropriate mitigations measure have been prescribed according to community impact.

Methodology

- LV / HV designated parking
- Emergency assembly point

Plant and equipment

- Generator
- Light vehicles
- Truck – medium rigid (20t)
- Watercart
- Lighting Towers
- Hydrema / Moxy

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime OOH:
  - 8am to 6pm Sunday and Public Holidays
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)

- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.3.2 Assessment

The additional work scenario has been assessed utilising SLR Predict. The plant and equipment list (as noted above) has been considered as a worst -case scenario within a 15-minute assessment period. The operating time (utilisation %) of each plant and equipment item is representative to site working conditions.

2.3.3 Results

The SLR Predict results are presented in Appendix C, for night out of hours, as the most affected period. Table 5 provides a summary of the exceedances identified through various assessments. It compares the following:

- W.002 exceedances identified in the Billy Hughes CNVIS
- W.002C exceedances identified in the SLR Predict results for the revised plant and equipment list for OOH night May Possession works.

TABLE 5: EXCEEDANCE COMPARISONS FOR W.002C

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.002 CNVIS	W.002C SLR Predict – revised work area
Total Lw (dBA)	113	113
Noticeable (1-5 dB)	0	1
Clearly Audible (6-15 dB)	0	0
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 5 shows that there is a slight increase in the number of residential receivers with NML exceedances in the noticeable range (1-5dB) resulting from the revised work area for W.002C.

2.4 Earthworks (W.004B)

2.4.1 Scope

The revised work area (Figure 2) consists of the work area identified in the endorsed CNVIS, additional area considered as part of the approved Project and additional work areas identified in the Billy Hughes Bridge CA (Doc No: 6-0052-210-EAP-B5-AS-0001). Two additional pieces of plant / equipment are also considered likely to be used in this scenario, compared to that assessed in the endorsed CNVIS (posi track, bobcat).

Methodology

- Bulk excavation
- Stockpiling

Plant and equipment

- Articulated Dump Truck

- Backhoe
- Crane (mobile)
- Excavator – Tracked (20t)
- Front End Loader
- Generator
- Grader
- Hand tools (electric)
- Light vehicles
- Plate Compactor
- Roller – Vibratory
- Telescopic Handler
- Truck – Medium Rigid (20t)
- Truck – Vacuum (NDD)
- Watercart
- Posi track
- Bobcat

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime out-of-hours (OOH)
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.4.2 Assessment

The revised work area has been assessed utilising SLR Predict. The highest noise generating items of plant and equipment in this work scenario (front end loader and grader) have been considered as a worst-case scenario with 100% utilisation within a 15-minute assessment period.

2.4.3 Results

The SLR Predict results are presented in Appendix D, for night time out of hours, as the most affected period. Table 6 provides a summary of the noise exceedances identified through various assessments. It compares the following:

- W.004 exceedances identified in the Billy Hughes CNVIS (original earthwork scenario)
- W.004B exceedances identified in the SLR Predict results for the revised work area shown in Figure 2.

TABLE 6: EXCEEDANCE COMPARISONS FOR W.004B

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.004 CNVIS	W.004B SLR Predict – revised work area
Total Lw (dBA)	117	116
Noticeable (1-5 dB)	0	0
Clearly Audible (6-15 dB)	1	2
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 6 shows that there are minimal changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.004B.

2.5 Earthworks (W.004C)

2.5.1 Scope

The following plant and equipment list has been collated for Billy Hughes Bridge during the ARTC May Possession 2026, commencing Friday 1st May to Tuesday 5th May. Works taking place outside standard construction hours, as defined under section L4.1 of the EPL (# 21984), have therefore been assessed for noise impact and appropriate mitigations measure have been prescribed according to community impact.

The following construction activities are programmed to take place throughout the ARTC Possession window

Methodology

- Bulk excavation
- Foundation treatment
- Formation layer placement
- Redundant drainage removal

Plant and equipment

- Articulated Dump Truck
- Excavator (40t)
- Excavator – Tracked (30T)
- Excavator + hydraulic hammer
- Front End Loader
- Grader
- Light Vehicles
- Roller – Vibratory
- Truck – Medium Rigid (20t)

- Watercart
- Posi Track
- Dozer
- Lighting Towers

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime out-of-hours (OOH)
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.5.2 Assessment

The additional work scenario has been assessed utilising SLR Predict. The plant and equipment list (as noted above) has been considered as a worst -case scenario within a 15-minute assessment period. The operating time (utilisation %) of each plant and equipment item is representative to site working conditions.

2.5.3 Results

The SLR Predict results are presented in Appendix E, for night time out of hours, as the most affected period. Table 7 provides a summary of the noise exceedances identified through various assessments. It compares the following:

- W.004 exceedances identified in the Billy Hughes CNVIS (original earthwork scenario)
- W.004B exceedances identified in the SLR Predict results for the revised work area shown in Figure 2.
- W.004C exceedances identified in the SLR Predict results for the revised plant and equipment list for OOH night May Possession works

TABLE 7: EXCEEDANCE COMPARISONS FOR W.004C

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE		
	W.004 CNVIS	W.004B SLR Predict – revised work area	W.004C SLR Predict revised plant and equipment
Total Lw (dBA)	117	116	122
Noticeable (1-5 dB)	0	0	4
Clearly Audible (6-15 dB)	1	2	2
Moderately Intrusive (16-25 dB)	0	0	0
Highly Intrusive (>25 dB)	0	0	0

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE		
	W.004 CNVIS	W.004B SLR Predict – revised work area	W.004C SLR Predict revised plant and equipment
Above Sleep Disturbance	n/a	1	1
Above Sleep Awake	n/a	0	0

Table 7 shows that the sound power level (Lw) has increased, with this being attributable to the amended plant and equipment list. There is an increase in the number of residential receivers experiencing noticeable (1-5dB) impacts resulting from the revised plant list for W.004C May Possession night works. However, it should be noted that the number of receivers experiencing above sleep disturbance impacts under W.004C with revised plant and equipment remains unchanged from W.004B assessed at Revision 3.

2.6 Track Work - Peak (W.005A)

2.6.1 Scope

The following plant and equipment list has been collated for Billy Hughes Bridge during the ARTC May Possession 2026, commencing Friday 1st May to Tuesday 5th May 2026. Works taking place outside standard construction hours, as defined under section L4.1 of the EPL (# 21984), have therefore been assessed for noise impact and appropriate mitigations measure have been prescribed according to community impact.

The following construction activities are programmed to take place throughout the ARTC Possession window

Methodology

- **Ballast excavation**
- **Sleeper removal**
- **Ballast and sleeper install**
- **Track slew**
- **Track install and welding**

Plant and equipment

- 30t **Excavator (Hi-Rail)**
- 40t **Excavator**
- **Pos**itrack
- 30t **Moxy (Hi-Rail)**
- P**adfoot Roller**
- **Smooth Drum Roller**
- **Front End Loader**
- **20KL Watercart**
- **Lighting towers**

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime out-of-hours (OOH)
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.6.2 Assessment

The additional work scenario has been assessed utilising SLR Predict. The plant and equipment list (as noted above) has been considered as a worst -case scenario within a 15-minute assessment period. The operating time (utilisation %) of each plant and equipment item is representative to site working conditions.

2.6.3 Results

The SLR Predict results are presented in Appendix F, for night time out of hours, as the most affected period. Table 8 provides a summary of the noise exceedances identified through various assessments. It compares the following:

- W.005 exceedances identified in the Billy Hughes CNVIS
- W.005A exceedances identified in the SLR Predict results for the revised plant and equipment list for OOH night May Possession works

TABLE 8: EXCEEDANCE COMPARISONS FOR W.005A

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.005 CNVIS	W.005A SLR Predict – revised work area
Total Lw (dBA)	119	118
Noticeable (1-5 dB)	2	1
Clearly Audible (6-15 dB)	2	1
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 8 shows a decreased number of receivers experiencing a noticeable level of noise (1-5 dB exceedance) and clearly audible level of noise ((6-15dB exceedance). There are no other changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.005A.

2.7 Retaining wall and protection barrier construction (W.009B)

2.7.1 Scope

A revision of the work area is not required for this work scenario at the Billy Hughes Bridge enhancement site. However, it was necessary to update the list of plant and equipment and to consider the evening OOH period following further construction planning.

Methodology

- Deflection wall construction
- Soil nail wall construction

Plant and equipment

- Compressor
- Concrete pencil vibrator
- Concrete pump truck
- Tracked Hydraulic Drilling Rig
- Scissor Lift
- Excavator – Tracked (20t)
- Generator
- Hand tools (electric)
- Hydraulic/pneumatic tools
- Light Vehicle
- Loader
- Plate Compactor
- Roller – smooth drum
- Saw – concrete
- Telescopic handler
- Truck – medium rigid (20t)
- Watercart

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime OOH
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays).

2.7.2 Assessment

The updated list of equipment and construction hours have been assessed utilising SLR Predict. The list of equipment and respective utilisation was replicated in SLR Predict, with 'Tracked Hydraulic Drilling Rig' added to the plant and equipment list with 30% utilisation within a 15-minute assessment period.

2.7.3 Results

The SLR Predict results are presented in Appendix G, for evening OOH, as the most affected period. Retaining wall and protection barrier construction will not be undertaken during night out of hours.

Table 9 provides a summary of the exceedances identified through various assessments. It compares the following:

- W.009 exceedances identified in the Billy Hughes CNVIS (original retaining wall and protection barrier construction work scenario) during daytime OOH
- W.009B exceedances identified in SLR Predict for the revised list of equipment during daytime OOH
- W.009B exceedances identified in SLR Predict for the revised list of equipment during evening OOH.

TABLE 9: EXCEEDANCE COMPARISONS FOR W.009B

ASSESSMENT RESULTS	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE		
	W.009 CNVIS (daytime OOH)	W.009B SLR Predict – revised equipment list (daytime OOH)	W.009B SLR Predict – revised equipment list (evening OOH)
Total Lw (dBA)	119	119	119
Noticeable (1-5 dB)	0	1	1
Clearly Audible (6-15 dB)	1	1	1
Moderately Intrusive (16-25 dB)	0	0	0
Highly Intrusive (>25 dB)	0	0	0

Table 9 shows that there are minimal changes in the number of residential receivers with NML exceedances resulting from the revised list of equipment and working hours for W.009. One additional receiver would experience a noticeable level of noise (1-5 dB exceedance) compared with the CNVIS, though the CNVIS highlights this receiver as being impacted by other activities at the Billy Hughes Bridge enhancement site. The proposed scenario and construction hours would result in a similar level of impact to affected receivers as that considered in the endorsed CNVIS.

2.8 Signalling enabling activities (W.011A)

2.8.1 Scope

The revised work area (Figure 5) required for Billy Hughes forms part of the wider scope associated at the Billy Hughes Bridge enhancement site and will enable signalling activities. The revised work area, which consists of the work area identified in the endorsed CNVIS and additional work areas identified in the Billy Hughes Bridge CA (Doc No: 6-0052-210-EAP-B5-AS-0001).

Methodology

- Access for cable pulling and testing works

Plant and equipment

- Hand tools (electric)
- Light vehicles

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.

- Daytime OOH
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.8.2 Assessment

The revised work area has been assessed utilising SLR Predict. The highest noise generating items of plant and equipment in this work scenario (light vehicles and powered hand tools) have been considered as a worst-case scenario with 100% utilisation within a 15-minute assessment period.

2.8.3 Results

The SLR Predict results are presented in Appendix H, for nighttime out of hours, as the most affected period. Table 10 provides a summary of the exceedances identified through various assessments. It compares the following:

- W.011 exceedances identified in the Billy Hughes CNVIS (original signalling work scenario)
- W.011A exceedances identified in the SLR Predict results for the revised work area shown in Figure 5.

TABLE 10: EXCEEDANCE COMPARISONS FOR W.011A

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.011 CNVIS	W.011A SLR Predict – revised work area
Total Lw (dBA)	113	106
Noticeable (1-5 dB)	1	0
Clearly Audible (6-15 dB)	0	0
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 10 shows a decreased number of receivers experiencing a noticeable level of noise (1-5 dB exceedance). There are no other changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.011A.

2.9 Installation of signalling infrastructure (W.011B)

2.9.1 Scope

The revised work area (Figure 6) required for Billy Hughes forms part of the wider scope associated at the Billy Hughes Bridge enhancement site and will enable signalling activities. The revised work area consists of the work area identified in the endorsed CNVIS and additional work areas identified in the Billy Hughes Bridge CA (Doc No: 6-0052-210-EAP-B5-AS-0001).

Methodology

- Installation of signalling infrastructure

Plant and equipment

- Crane (mobile)
- Directional drill
- Elevated work platform
- Excavator – Tracked (20t)
- Generator
- Hand tools (electric)
- Light vehicle
- Telescopic handler
- Truck – medium rigid (20t)
- Truck – vacuum (NDD)
- Wacker packer

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime OOH
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.9.2 Assessment

The revised work area has been assessed utilising SLR Predict. The highest noise generating items of plant and equipment in this work scenario (truck – vacuum (NDD) and directional drill) have been considered as a worst-case scenario with 100% utilisation within a 15-minute assessment period.

2.9.3 Results

The SLR Predict results are presented in Appendix I, for nighttime out of hours, as the most affected period. Table 11 provides a summary of the exceedances identified through various assessments. It compares the following:

- W.011 exceedances identified in the Billy Hughes CNVIS (original signalling work scenario)
- W.011B exceedances identified in the SLR Predict results for the revised work area shown in Figure 6.

TABLE 11: EXCEEDANCE COMPARISONS FOR W.011B (DIRECTIONAL DRILL)

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.011 CNVIS	W.011B SLR Predict – revised work area (directional drill)
Total Lw (dBA)	113	101
Noticeable (1-5 dB)	1	0
Clearly Audible (6-15 dB)	0	0

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.011 CNVIS	W.011B SLR Predict – revised work area (directional drill)
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 11 shows a decreased number of receivers experiencing a noticeable level of noise (1-5 dB exceedance). There are no other changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.011B.

TABLE 12: EXCEEDANCE COMPARISONS FOR W.011B (VACUUM TRUCK)

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.011 CNVIS	W.011B SLR Predict – revised work area (vacuum truck)
Total Lw (dBA)	113	109
Noticeable (1-5 dB)	1	0
Clearly Audible (6-15 dB)	0	0
Moderately Intrusive (16-25 dB)	0	0
Highly Intrusive (>25 dB)	0	0

Table 12 shows a decreased number of receivers experiencing a noticeable level of noise (1-5 dB exceedance). There are no other changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.011B.

2.10 Earthworks (W.011C)

2.10.1 Scope

The following plant and equipment list has been collated for Billy Hughes Bridge during the ARTC May Possession 2026, commencing Friday 1st May to Tuesday 5th May. Works taking place outside standard construction hours, as defined under section L4.1 of the EPL (# 21984), have therefore been assessed for noise impact and appropriate mitigations measure have been prescribed according to community impact.

The following construction activities are programmed to take place throughout the ARTC Possession window

Methodology

- **Disconnecting and reconnecting of signalling cables**
- **Testing of signalling functions post relocation**

Plant and equipment

- **Light Vehicles**
- **Hand Tools Electric**

Construction hours

- Standard approved construction hours:
  - 7am to 6pm Monday to Friday, inclusive
  - 7am to 6pm Saturday.
- Daytime out-of-hours (OOH)
  - 8am to 6pm Sunday and Public Holidays.
- Evening OOH:
  - 6pm to 10pm Monday to Sunday (including Public Holidays)
- Night OOH:
  - 10pm to 7am Monday to Saturday
  - 10pm to 8am Sunday (including Public Holidays)

2.10.2 Assessment

The additional work scenario has been assessed utilising SLR Predict. The plant and equipment list (as noted above) has been considered as a worst -case scenario within a 15-minute assessment period. The operating time (utilisation %) of each plant and equipment item is representative to site working conditions.

2.10.3 Results

The SLR Predict results are presented in Appendix J, for night time out of hours, as the most affected period. Table 13 provides a summary of the noise exceedances identified through various assessments. It compares the following:

- W.011 exceedances identified in the Billy Hughes CNVIS
- W.011C exceedances identified in the SLR Predict results for the revised plant and equipment list for OOH night May Possession works

TABLE 13: EXCEEDANCE COMPARISONS FOR W.011C

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.011 CNVIS	W.011C SLR Predict – revised work area
Total Lw (dBA)	113	104
Noticeable (1-5 dB)	1	0
Clearly Audible (6-15 dB)	0	0
Moderately Intrusive (16-25 dB)	0	0

ASSESSMENT RESULTS (NIGHT OOH)	NUMBER OF RESIDENTIAL RECEIVERS WITH NML EXCEEDANCE	
	W.011 CNVIS	W.011C SLR Predict – revised work area
Highly Intrusive (>25 dB)	0	0

Table 13Table 10 shows a decreased number of receivers experiencing a noticeable level of noise (1-5 dB exceedance) and clearly audible level of noise ((6-15dB exceedance). There are no other changes in the number of residential receivers with NML exceedances resulting from the revised work area for W.011C.

3 VIBRATION ASSESSMENT

3.1 Site establishment activities (W.001B)

There are no vibration intensive plant and equipment proposed as part of W.001B; therefore, no vibration impacts are expected.

3.2 Compound operation activities (W.002B)

There are no vibration intensive plant and equipment proposed as part of W.002B; therefore, no vibration impacts are expected.

3.3 Earthworks (W.004B)

A 7-13 tonne vibratory roller is proposed for use in the W.004B scenario. The W.004 scenario does not result in the potential exceedance of the cosmetic damage or human comfort criteria at any identified structures, as shown in Figure 4 of the CNVIS (Doc No. 6-0052-210-EEC-B5-AS-0001).

This CNVIS Addendum considers the change in equipment location resulting from the expanded work areas assessed in scenario W.004B. A review of the vibration results for scenario W.004B can be found in Appendix D. The criteria for human comfort is potentially exceeded at one non-residential property.

3.4 Earthworks (W.004C)

The following vibration-intensive plant will be utilised for W.004C:

- 4 x 7-13 tonne vibratory rollers
- 1 x Excavator with Hammer Attachment (>30T)

The W.004C scenario does not result in the potential exceedance of the cosmetic damage or human comfort criteria at any identified structures, as shown in Figure 4 of the CNVIS (Doc No. 6-0052-210-EEC-B5-AS-0001).

A review of the vibration results for May possession scenario W.004C can be found in Appendix E.

3.5 Retaining walls and protection barrier construction (W.009B)

There are no vibration intensive plant and equipment proposed as part of W.009B; therefore, no vibration impacts are expected.

3.6 Signalling enabling activities (W.011A)

There are no vibration intensive plant and equipment proposed as part of W.011A; therefore, no vibration impacts are expected.

3.7 Installation of signalling infrastructure (W.011B)

There are no vibration intensive plant and equipment proposed as part of W.011B; therefore, no vibration impacts are expected.

4 CONCLUSION

4.1 Mitigation and management measures

As this Addendum forms part of the endorsed CNVIS for Billy Hughes the same mitigation and management measures apply as noted in Section 8 of the CNVIS.

4.2 Additional mitigation measures

As noted in Figure 7 to Figure 9 and under Appendix A to Appendix F, the SLR Predict results include a section on all applicable additional mitigation measures. There additional mitigation measures will be implemented where appropriate.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	Exceedance of NML	Perception	Duration	Communication Category/Management Measure
OOHW Daytime PeriodSunday 7am - 6pm(including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening PeriodMonday - Sunday 6pm - 10pm(including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night PeriodMonday - Sunday 10pm - 7am(including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

FIGURE 7: ADDITIONAL MITIGATION MEASURES MATRIX - NOISE

Vibration - Additional Mitigation Measures Matrix			
Time Period	Duration	Exceedance of 'preferred' value	Exceedance of 'maximum' value
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

FIGURE 8: ADDITIONAL MITIGATION MEASURES MATRIX - VIBRATION

Additional Mitigation Measures	
Measure	Abbreviation
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.

Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.

Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	Description	Code	Description
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

FIGURE 9: ADDITIONAL MITIGATION MEASURES MATRIX - NOTES



APPENDICES

APPENDIX A

SLR Predict Results (W.001B) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	Copy of W.001 B - BHB - Revised working area
Stage	A2I Construction
Permit Number	NA
Start Date	2025-10-10
End Date	2025-10-24
Assessment Period	Day - out of hours

Equipment Details

Plant/Equipment	**Equipment Sound Power Level (Unadjusted), dBA**	**Number of Units**	**Temporary Noise Barrier**
1: Scenario W.001 (Height: Ground)	Total: 114		
Articulated Dump Truck 100% operation	109	1	No
Front End Loader 100% operation	113	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	1 property	0 property
Noticeable	1 property	0 property

Legend

Project Boundary
Work Areas
Barriers

Results by Receiver

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category
19 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	52	10	Clearly Audible
43 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	46	4	Noticeable

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.

Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.

Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX B

SLR Predict Results (W.002B) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels

The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses 'realistic worst-case' scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	W.002b Site Compound BHB - 04.007 May Possession
Assessment Number	431
Stage	A2I Construction
Permit Number	W.002b / 04.007
Start Date	2026-05-01
End Date	2026-04-05
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: W.002b Site Compound (Height: Ground)	Total: 108		
Generator - diesel/ petrol 100% operation	103	1	No
Truck - medium rigid (20T) 25% operation	103	1	No
Water Cart 100% operation	105	1	No
Lighting Tower 100% operation	80	6	No
Light Vehicle (steady state) 25% operation	87	30	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	0 property	0 property
Noticeable	0 property	0 property
Above Sleep Disturbance	0 property	0 property
Above Sleep Awake	0 property	0 property

Legend

Project Boundary	
Work Areas	
Barriers	

Results by Receiver

Facade/Floor: Show, Minimum floor to show: 0

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category

No results

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**

OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures

Measure	Abbreviation
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types

Code	Description	Code	Description
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX C

SLR Predict Results (W.002C) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).
Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.
Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers
In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels
The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses 'realistic worst-case' scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	W.002C BHB Compound operations
Assessment Number	478
Stage	A2I Construction
Permit Number	04.007 V1
Start Date	2026-05-01
End Date	2026-05-05
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: (Height: Ground)	Total: 113		
Generator - diesel/ petrol 100% operation	103	1	No
Light Vehicle (steady state) 25% operation	87	30	No
Lighting Tower 100% operation	80	6	No
Truck - medium rigid (20T) 25% operation	103	1	No
Water Cart 100% operation	105	1	No
Hydrema / Moxy 80% operation	107	4	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



		Residential	Non-Residential
	Highly Intrusive	0 property	0 property
	Moderately Intrusive	0 property	0 property
	Clearly Audible	0 property	0 property
	Noticeable	1 property	0 property
	Above Sleep Disturbance	0 property	0 property
	Above Sleep Awake	0 property	0 property

Legend

	Project Boundary
	Work Areas
	Barriers

Results by Receiver

Facade/Floor: Show, Minimum floor to show: 0

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category
19 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	47	5	Noticeable

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO

OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures

Measure	Abbreviation
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types

Code	Description	Code	Description
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX D

SLR Predict Results (W.004B) Noise and Vibration

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels

The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses 'realistic worst-case' scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	W.004b BHB - Earthworks, 04.007 May Possession
Assessment Number	432
Stage	A2I Construction
Permit Number	04.007 / W.004b
Start Date	2026-05-01
End Date	2026-05-05
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	**Equipment Sound Power Level (Unadjusted), dBA**	**Number of Units**	**Temporary Noise Barrier**
1: W.004b - 04.007 (Height: Ground)	Total: 122		
Excavator - Tracked (40T) 50% operation	115	1	No
Hydrema / Moxy 25% operation	107	10	No
Grader (large) 50% operation	113	2	No
Positrack 50% operation	104	2	No
Dozer (CAT D9) 50% operation	116	1	No
Truck - medium rigid (20T) 25% operation	103	3	No
Roller - vibratory (7-13t) 100% operation	109	4	No


Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
Front End Loader 50% operation	113	2	No
Water Cart 75% operation	105	2	No
Light Vehicle (steady state) 25% operation	87	10	No
Lighting Tower 100% operation	80	24	No
Excavator 10T + hydraulic hammer 30% operation	118	2	No
Excavator - Tracked (30T) 50% operation	110	2	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results

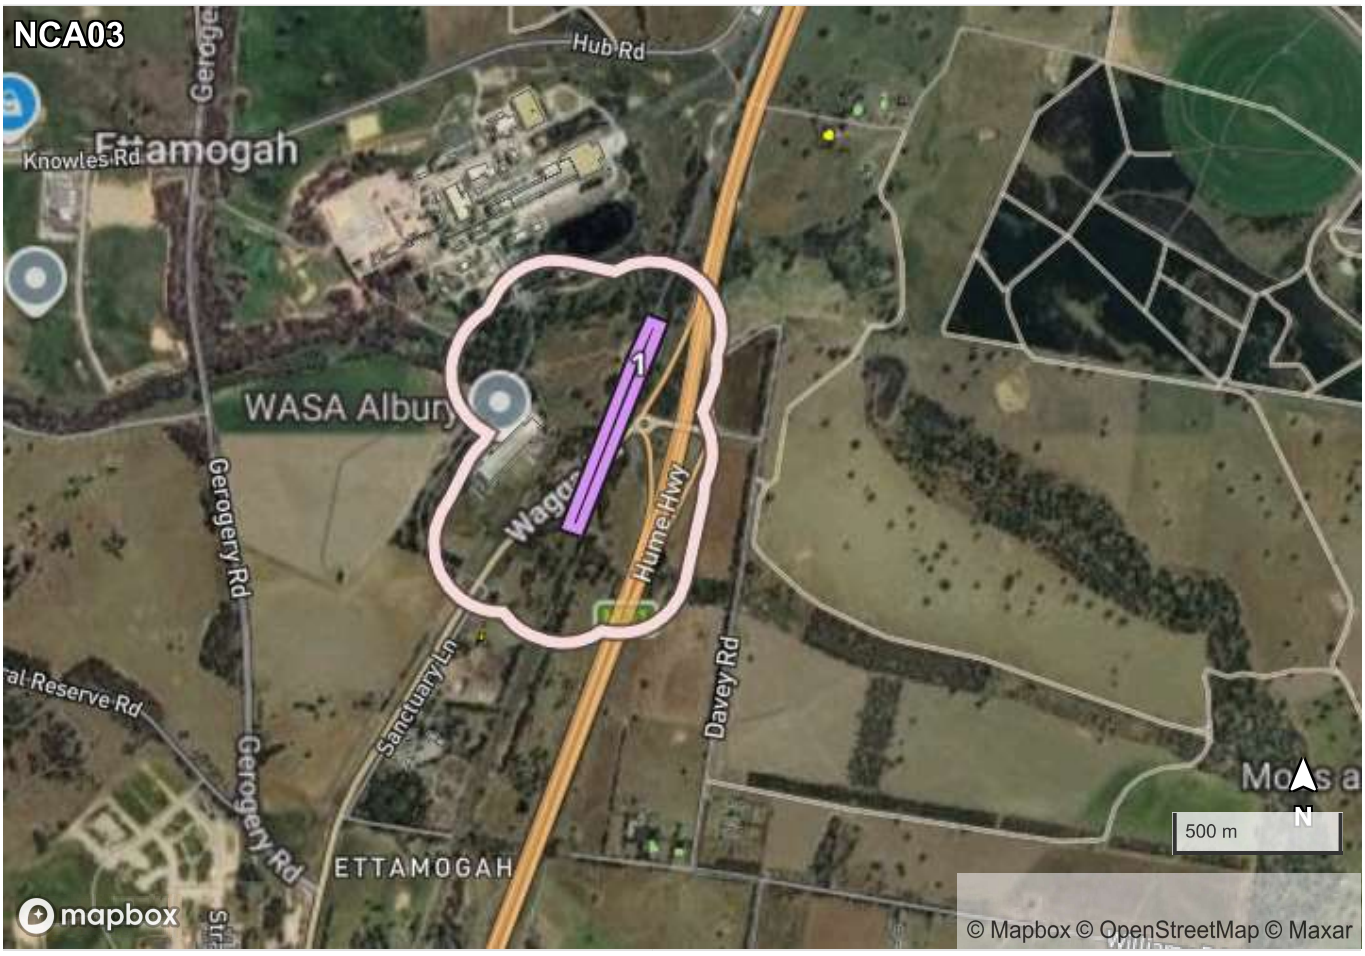

Assessment Results

	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	2 properties	0 property
Noticeable	4 properties	0 property
Above Sleep Disturbance	1 property	0 property
Above Sleep Awake	0 property	0 property

Legend

Project Boundary
Work Areas
Barriers

Results by Receiver

Facade/Floor: Show, Minimum floor to show: 0

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category
19 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	55	13	Clearly Audible Above Sleep Dist
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	49	7	Clearly Audible
214 WILLIAMS RD, TABLE TOP NSW 2640	RES	NCA03	42	46	4	Noticeable
206 WILLIAMS RD, TABLE TOP NSW 2640	RES	NCA03	42	45	3	Noticeable
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	44	2	Noticeable
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	43	1	Noticeable

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**

OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures

Measure	Abbreviation
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types

Code	Description	Code	Description
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX E

SLR Predict Results (W.004C) Noise and Vibration

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).
Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.
Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers
In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels
The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses 'realistic worst-case' scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	W.004C BHB - Earthworks, 04.007 May Possession
Assessment Number	432
Stage	A2I Construction
Permit Number	04.007 / W.004b
Start Date	2026-05-01
End Date	2026-05-05
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: W.004C - 04.007 (Height: Ground)	Total: 122		
Excavator - Tracked (40T) 50% operation	115	1	No
Hydrema / Moxy 25% operation	107	10	No
Grader (large) 50% operation	113	2	No
Positrack 50% operation	104	2	No
Dozer (CAT D9) 50% operation	116	1	No
Truck - medium rigid (20T) 25% operation	103	3	No
Roller - vibratory (7-13t) 100% operation	109	4	No
Front End Loader 50% operation	113	2	No
Water Cart 75% operation	105	2	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
Light Vehicle (steady state) 25% operation	87	10	No
Lighting Tower 100% operation	80	24	No
Excavator 10T + hydraulic hammer 30% operation	118	2	No
Excavator - Tracked (30T) 50% operation	110	2	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	2 properties	0 property

Assessment Results

	Noticeable	4 properties	0 property
	Above Sleep Disturbance	1 property	0 property
	Above Sleep Awake	0 property	0 property

Legend

	Project Boundary
	Work Areas
	Barriers

Results by Receiver

Facade/Floor: Show, Minimum floor to show: 0

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category
19 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	55	13	Clearly Audible Above Sleep Dist
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	49	7	Clearly Audible
214 WILLIAMS RD, TABLE TOP NSW 2640	RES	NCA03	42	46	4	Noticeable
206 WILLIAMS RD, TABLE TOP NSW 2640	RES	NCA03	42	45	3	Noticeable
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	44	2	Noticeable
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	43	1	Noticeable

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO

OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures

Measure	Abbreviation
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types

Code	Description	Code	Description
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).
Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.
Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers
In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels
The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses 'realistic worst-case' scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details


Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	04.007 - BHB OOH May Possession 2026 (vibration)
Assessment Number	456
Stage	A2I Construction
Permit Number	04.007 v1
Start Date	2026-05-01
End Date	2026-05-05
Assessment Period	Vibration

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: (Height: Ground)	Total: 120		
Roller - vibratory (7-13t) 100% operation	109	4	No
Excavator 10T + hydraulic hammer 100% operation	118	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results

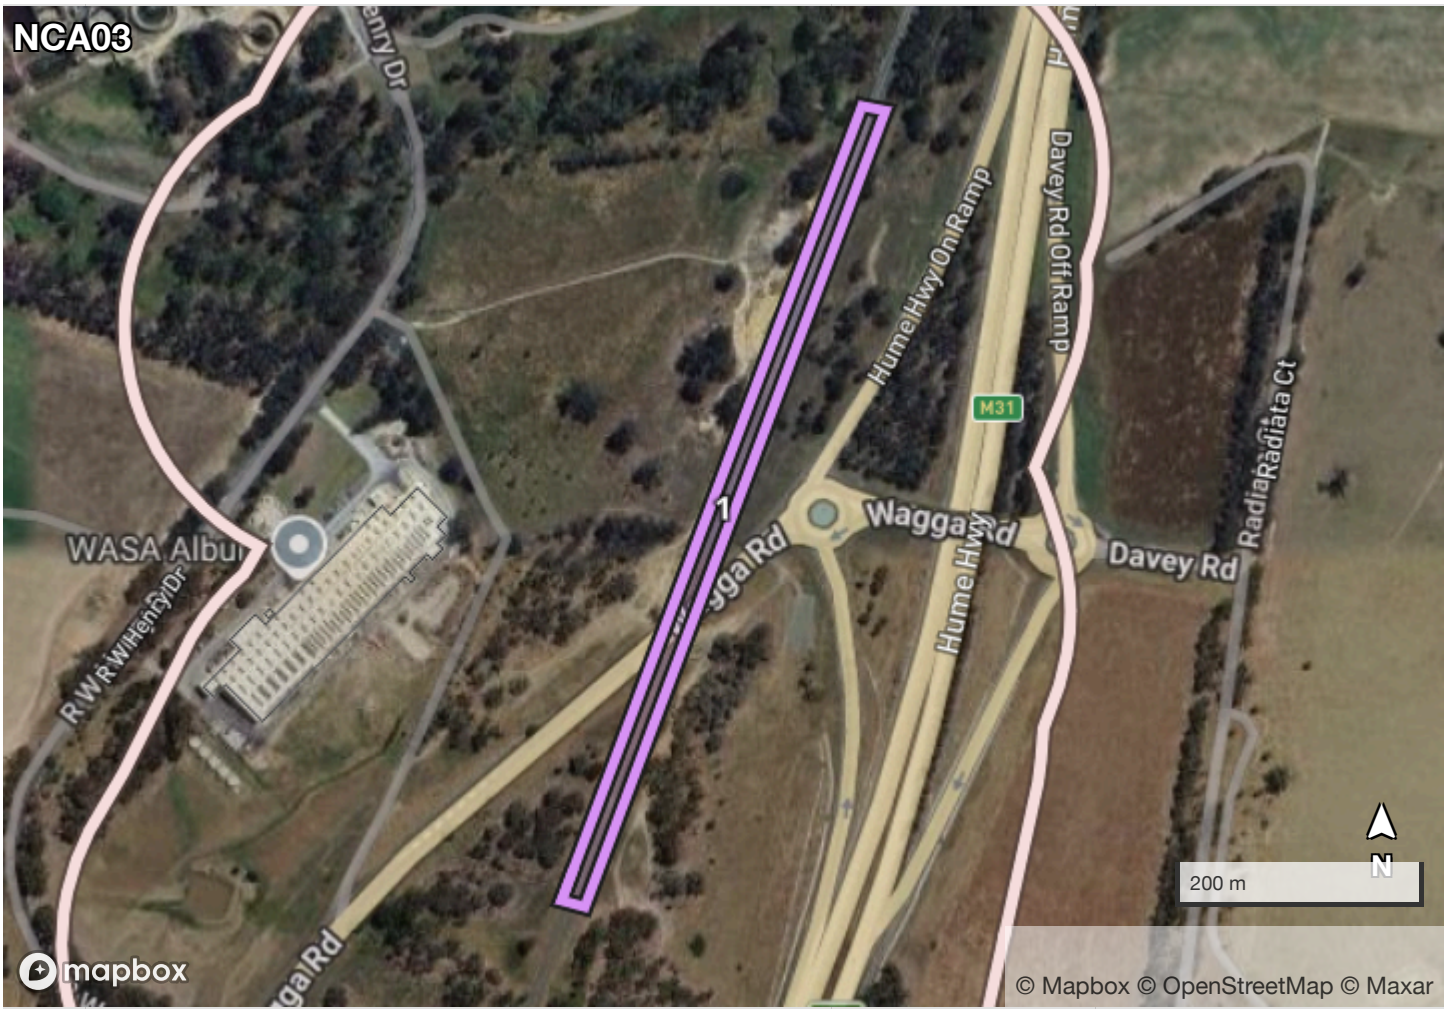

		Residential	Non-Residential
	Cosmetic Damage	0 property	0 property
	Human Comfort	0 property	0 property
	Cosmetic Damage for Unsound Heritage	0 property	0 property

Legend

	Project Boundary
	Work Areas
	Barriers

Results by Receiver

Address	Land Use	Vibration Category

No results

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO

OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures

Measure	Abbreviation
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types

Code	Description	Code	Description
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX F

SLR Predict Results (W.005A) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).
Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.
Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers
In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels
The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses ‘realistic worst-case’ scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	W.005 BHB - Track Work-Peak, 04.007 May Possession
Assessment Number	433
Stage	A2I Construction
Permit Number	04.007 - W.005
Start Date	2026-05-01
End Date	2026-04-05
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: W.005 Track Work - Peak (Height: Ground)	Total: 118		
Excavator - Tracked (40T) 50% operation	115	1	No
Excavator - Tracked (30T) 50% operation	110	2	No
Positrack 50% operation	104	1	No
Hi-Rail Hydrema 25% operation	107	2	No
Roller - vibratory (7-13t) 100% operation	109	2	No
Front End Loader 50% operation	113	1	No
Water Cart 75% operation	105	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
Lighting Tower 100% operation	80	5	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



		Residential	Non-Residential
	Highly Intrusive	0 property	0 property
	Moderately Intrusive	0 property	0 property
	Clearly Audible	1 property	0 property
	Noticeable	1 property	0 property
	Above Sleep Disturbance	0 property	0 property

Assessment Results

	Above Sleep Awake	0 property	0 property

Legend

	Project Boundary
	Work Areas
	Barriers

Results by Receiver

Facade/Floor: Show, Minimum floor to show: 0

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category
19 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	50	8	Clearly Audible
20 PLANTATION LANE, TABLE TOP NSW 2640	RES	NCA03	42	45	3	Noticeable

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**

OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX G

SLR Predict Results (W.009B) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	SD Revised working area W.009B - BHB
Stage	A2I Construction
Permit Number	NA
Start Date	2025-10-10
End Date	2025-10-24
Assessment Period	Day - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: W.009B (Height: Ground)	Total: 119		
Compressor 50% operation	109	1	No
Concrete pencil vibrator 100% operation	103	1	No
Concrete pump truck 100% operation	108	1	No
Elevated Work Platform - Scissor Lift 30% operation	98	1	No
Excavator - Tracked (20T) 50% operation	105	1	No
Generator - diesel/ petrol 100% operation	103	1	No
Hand tools (electric) 75% operation	102	2	No
Hydraulic / Pneumatic Tools 75% operation	116	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
Light Vehicle (accelerating) 25% operation	95	2	No
Loader - skidsteer (1T) 50% operation	110	1	No
Compactor (plate) 100% operation	104	1	No
Saw - concrete 25% operation	118	1	No
Truck - medium rigid (20T) 25% operation	103	2	No
Water Cart 75% operation	107	1	No
Telescopic Handler 50% operation	99	1	No
Tracked Hydraulic Drilling Rig 30% operation	109	1	No
Roller - static 100% operation	107	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	1 property	0 property
Noticeable	1 property	0 property

Legend

Project Boundary
Work Areas
Barriers

Results by Receiver

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category
19 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	50	8	Clearly Audible
43 SANCTUARY LANE, ETTAMOGAH NSW 2640	RES	NCA03	42	43	1	Noticeable

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix

Time Period	Exceedance of NML	Perception	Duration	Communication Category/Management Measure
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.

Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.

Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX H

SLR Predict Results (W.011A) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Assessment Details

Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	Billy Hughes Bridge CNVIS Addendum (Signalling W.011a)
Stage	A2I Construction
Permit Number	N/A
Start Date	2025-10-15
End Date	2025-10-15
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: Work Area 1 (Height: Ground)	Total: 106		
Light Vehicle (accelerating) 100% operation	95	3	No
Hand tools (electric) 100% operation	102	2	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results



	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	0 property	0 property
Noticeable	0 property	0 property
Above Sleep Disturbance	0 property	0 property
Above Sleep Awake	0 property	0 property

Legend

Project Boundary	
Work Areas	
Barriers	

Results by Receiver

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category

No results

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix

Time Period	Exceedance of NML	Perception	Duration	Communication Category/Management Measure
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.

Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.

Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX I

SLR Predict Results (W.011B) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Assessment Details


Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	Billy Hughes Bridge CNVIS Addendum (Signalling W.011b)
Stage	A2I Construction
Permit Number	N/A
Start Date	2025-10-15
End Date	2025-10-15
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: Work Area 1 (Height: Ground)	Total: 101		
Directional Drill 100% operation	101	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results

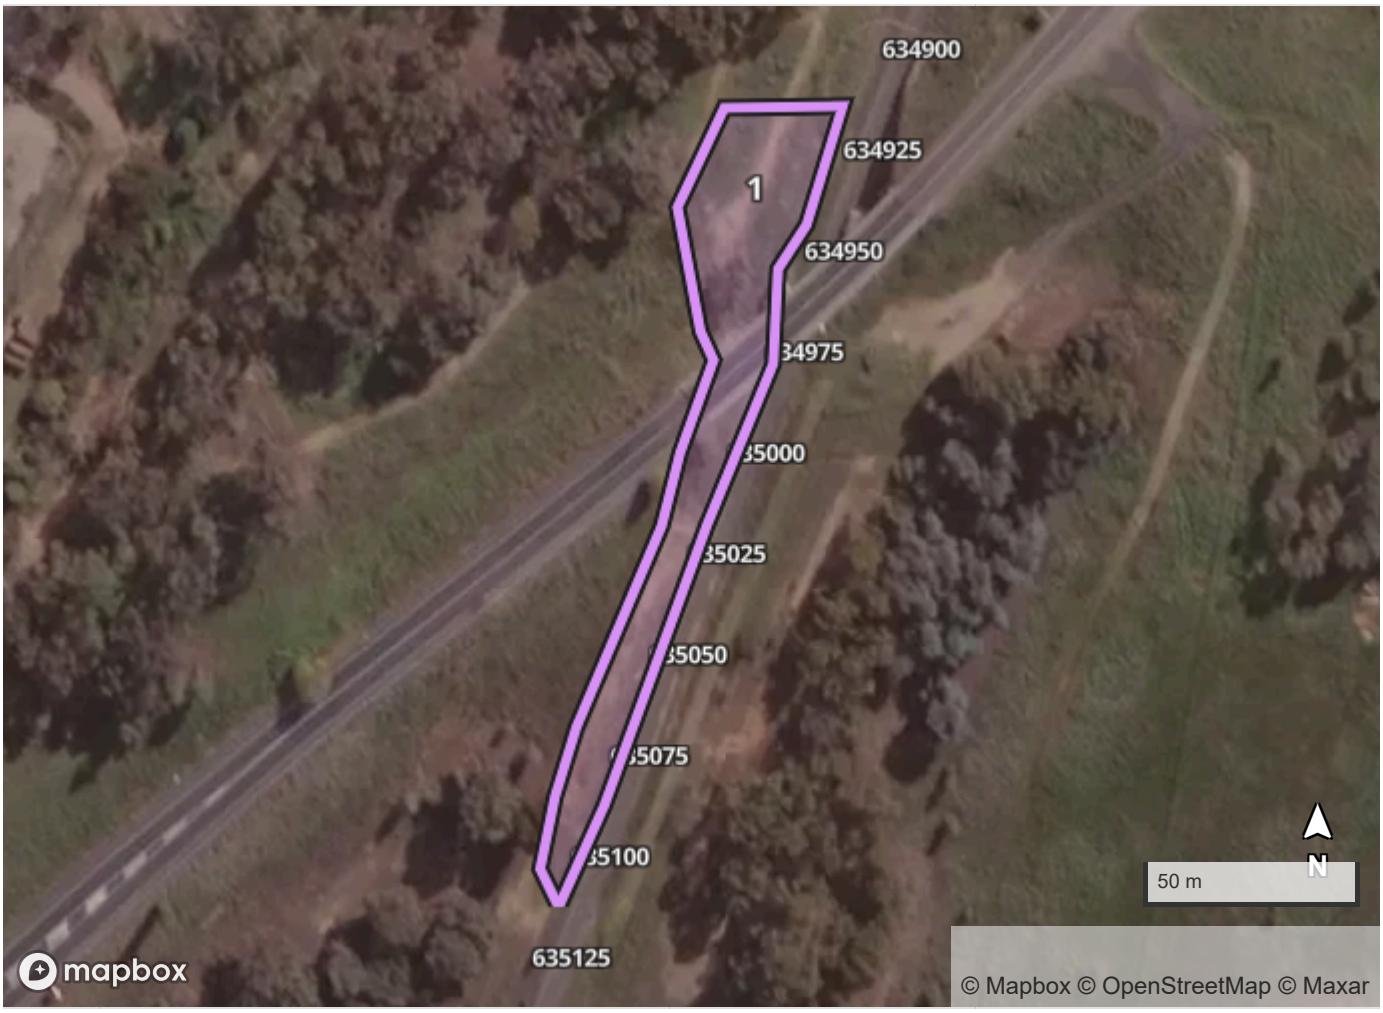

	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	0 property	0 property
Noticeable	0 property	0 property
Above Sleep Disturbance	0 property	0 property
Above Sleep Awake	0 property	0 property

Legend

Project Boundary	
Work Areas	
Barriers	

Results by Receiver

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category

No results

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix

Time Period	Exceedance of NML	Perception	Duration	Communication Category/Management Measure
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.
Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.
Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).

Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.

Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers

In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Assessment Details


Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	Billy Hughes Bridge CNVIS Addendum (Signalling W.011b)
Stage	A2I Construction
Permit Number	N/A
Start Date	2025-10-15
End Date	2025-10-15
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	Equipment Sound Power Level (Unadjusted), dBA	Number of Units	Temporary Noise Barrier
1: Work Area 1 (Height: Ground)	Total: 109		
Truck - vacuum (NDD or non-destructive digger) 100% operation	109	1	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results

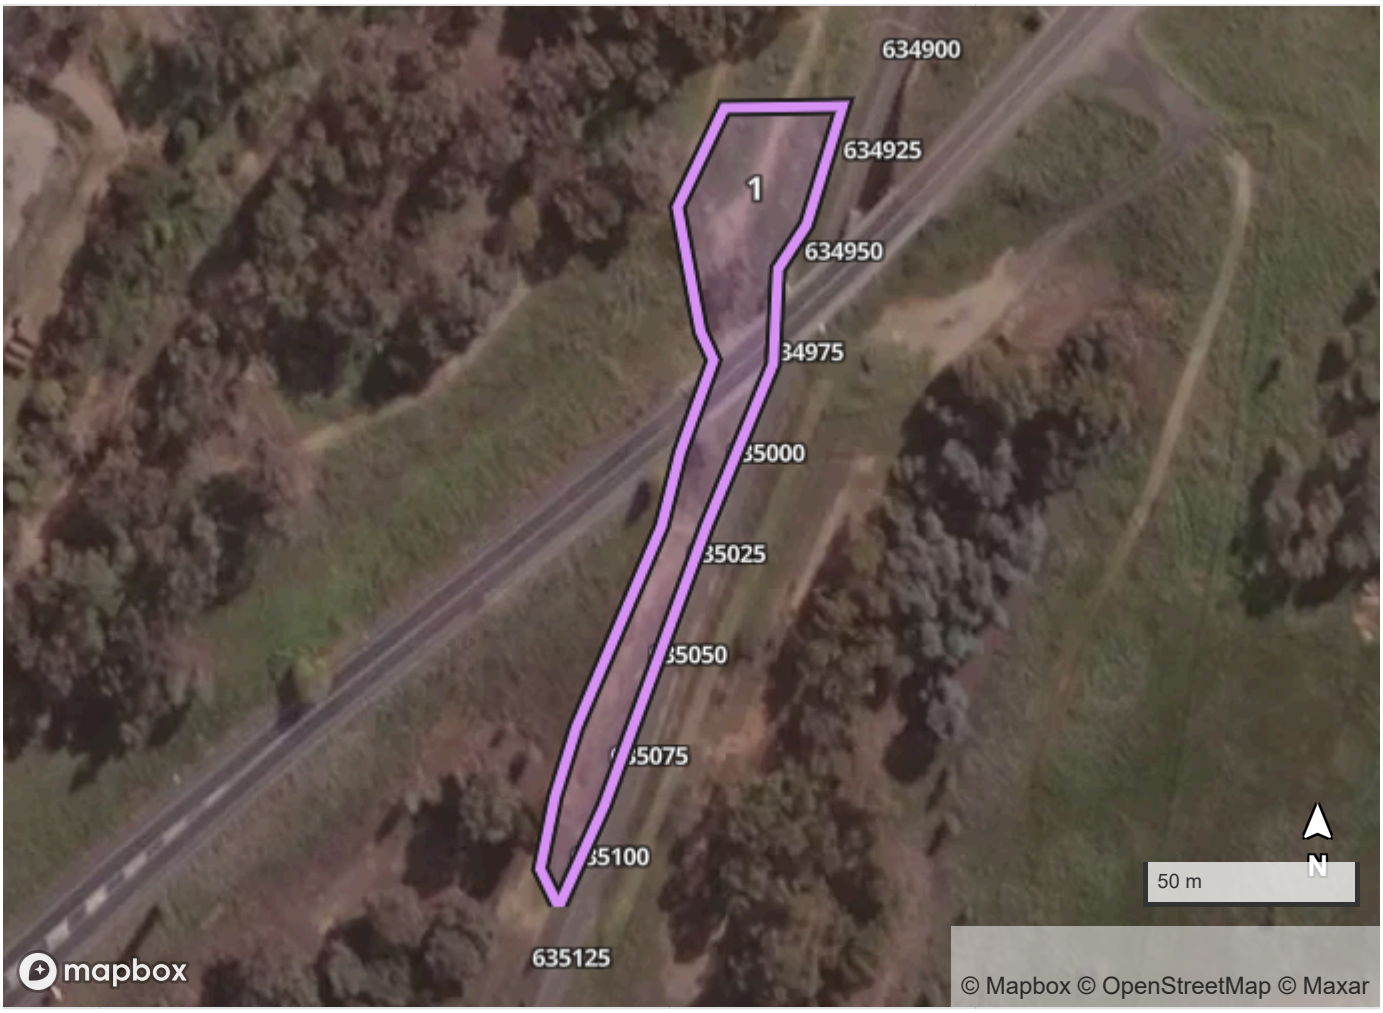

	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	0 property	0 property
Noticeable	0 property	0 property
Above Sleep Disturbance	0 property	0 property
Above Sleep Awake	0 property	0 property

Legend

Project Boundary	
Work Areas	
Barriers	

Results by Receiver

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category

No results

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix

Time Period	Exceedance of NML	Perception	Duration	Communication Category/Management Measure
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.

Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.

Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building

APPENDIX J

SLR Predict Results (W.011C) Noise

Construction Noise and Vibration Impact Statement (CNVIS)

This report presents the outcomes of detailed noise/vibration modelling relating to specific construction activities proposed on site in accordance with the methodology outlined in the *Construction Noise and Vibration Management Plan* (CNVMP) and overarching *Construction Noise and Vibration Impact Statement* (CNVIS).
Prior to detailed noise/vibration modelling being undertaken, work activities are reviewed and considered in relation to industry best practice, consistent with the requirements of the CNVMP. Consideration is first given to eliminating the noise/vibration emissions so far as reasonably practicable. Where elimination is not practicable, efforts are been made to reduce the risk as far as practical by implementing noise and vibration management measures as outlined in the overarching CNVIS and CNVMP.
Examples of these measures include selecting the quietest equipment and processes to complete the works, considering staging and periods of respite to minimise prolonged periods of noise and vibration exposure, and maximising distances between construction activities and sensitive receivers.

Consultation with Affected Receivers
In accordance with CoA E78, the CNVIS must include specific mitigation measures identified through consultation with affected sensitive land user(s) and the mitigation measures must be implemented for the duration of the Work. Details of this consultation are provided in the overarching CNVIS for each enhancement site.

Predicted Noise Levels
The assessment presents the highest predicted level at each receiver building, considering predictions at each floor and façade from all potential work areas. The assessment is generally considered conservative as the calculations assume several items of construction equipment are in use at the same time within each work area. The assessment uses 'realistic worst-case' scenarios to determine the impacts from the noisiest 15-minute period that is likely to occur for each work scenario.

Assessment Details


Author Name	
Author Email	noiseassessments@martinus.com.au
Author Organisation	Martinus Rail
Project Name	A2I - Albury to Illabo
Assessment Name	W.011 BHB - Signalling - 04.007 May Possession
Assessment Number	434
Stage	A2I Construction
Permit Number	04.007 - W.011
Start Date	2026-05-01
End Date	2026-04-05
Assessment Period	Night - out of hours

Equipment Details

Plant/Equipment	**Equipment Sound Power Level (Unadjusted), dBA**	**Number of Units**	**Temporary Noise Barrier**
1: W.011 Signalling (Height: Ground)	Total: 104		
Light Vehicle (steady state) 25% operation	87	3	No
Hand tools (electric) 75% operation	102	2	No

Note 1: Equipment classed as 'annoying' in the *Interim Construction Noise Guideline (DECC, 2009)* include a 5 dB correction.
Note 2: Equipment sound power levels consider the mitigation measures outlined in the overarching CNVIS to provide mitigated results.

Assessment Results

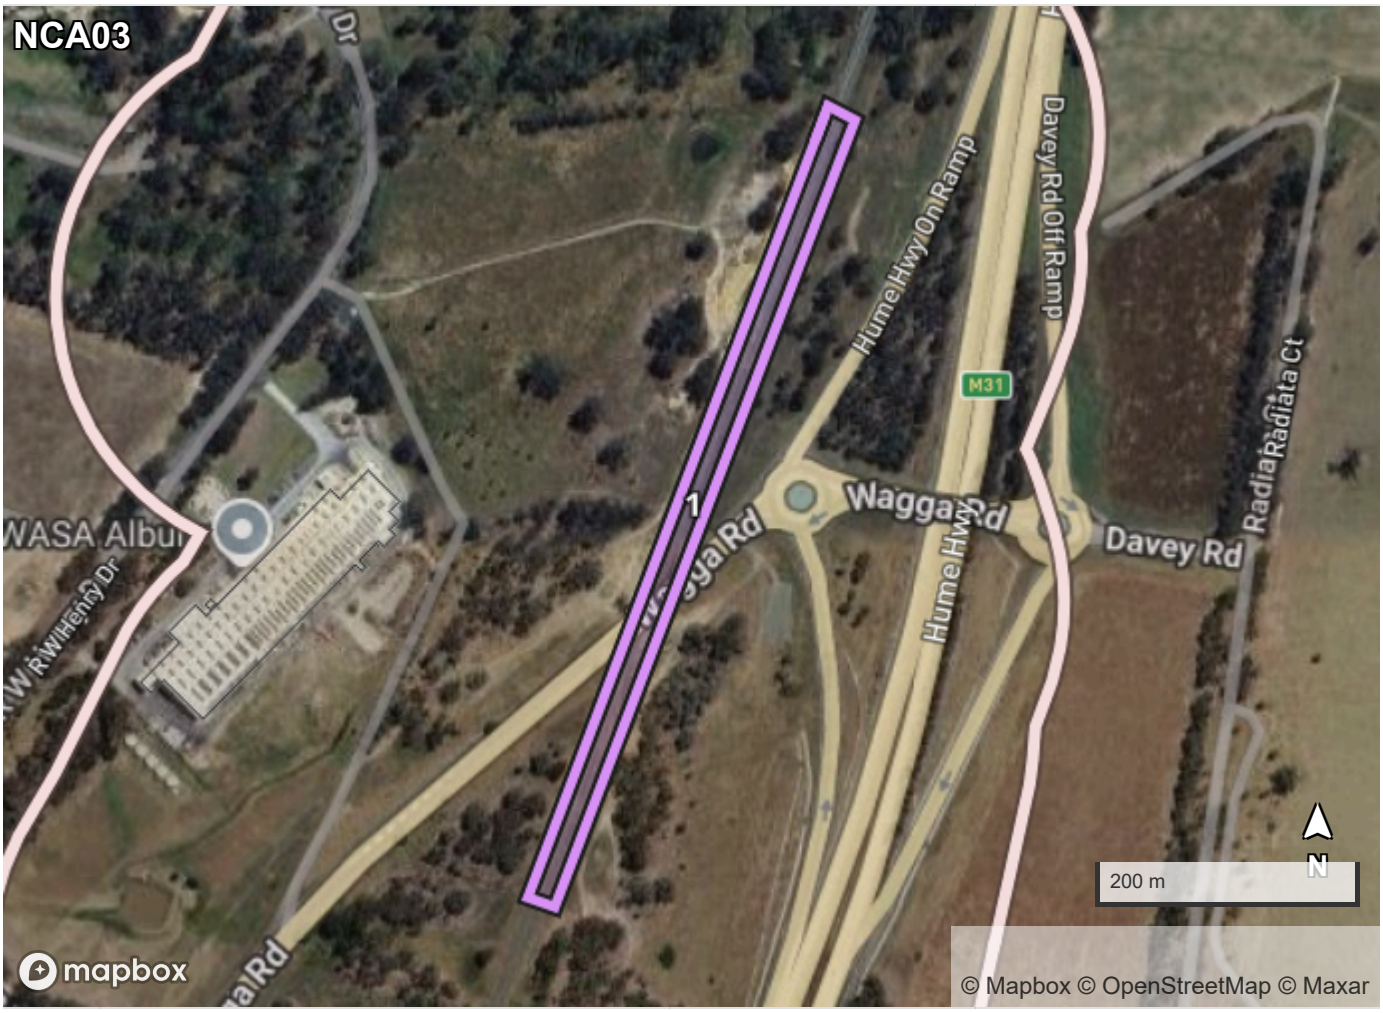

	Residential	Non-Residential
Highly Intrusive	0 property	0 property
Moderately Intrusive	0 property	0 property
Clearly Audible	0 property	0 property
Noticeable	0 property	0 property
Above Sleep Disturbance	0 property	0 property
Above Sleep Awake	0 property	0 property

Legend

Project Boundary	
Work Areas	
Barriers	

Results by Receiver

Address	Land Use	Noise Catchment Area	Construction Noise Management Level, dBA	Predicted Noise Level, dBA	Predicted Noise Level Above Noise Management Level, dB	Noise Category

No results

Recommended Mitigation Measures

This assessment has been conducted with regard to the relevant CNVIS and CNVMP. To manage noise and vibration impacts, project specific mitigation measures may be considered such as reviewing construction staging methodology to identify opportunities to schedule intensive works during less sensitive time periods and by providing a clear process for community engagement and complaints. Likewise, the requirements and actionable items within the overarching CNVIS and CNVMP should be considered and adopted where appropriate. Following the consideration of project specific noise mitigation measures, additional noise mitigation measures to be explored are described in the Inland Rail NSW Construction Noise and Vibration Framework (CNVF) and summarised below.

Airborne Noise - Additional Mitigation Measures Matrix				
Time Period	**Exceedance of NML**	**Perception**	**Duration**	**Communication Category/Management Measure**
OOHW Daytime Period Sunday 7am - 6pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
OOHW Evening Period Monday - Sunday 6pm - 10pm (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
	>25	Highly intrusive	Any	CO1, CO2
			>2 consecutive rest periods	CO1, CO2, RO
OOHW Night Period Monday - Sunday 10pm - 7am (including public holidays)	<5	Noticeable	Any	CO1
	5 - 15	Clearly audible	Any	CO1
	16 - 25	Moderately intrusive	Any	CO1, CO2
			>2 consecutive sleep periods	CO1, CO2, RO, AO
	>25	Highly intrusive	Any	CO1, CO2, RO
			>2 consecutive sleep periods	CO1, CO2, RO, AO, AltA

Vibration - Additional Mitigation Measures Matrix			
Time Period	**Duration**	**Exceedance of 'preferred' value**	**Exceedance of 'maximum' value**
OOHW Daytime Period Sunday 8am-6pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Evening Period Mon-Sun 6pm-10pm	Any	CO1, CO2	CO1, CO2, RO
OOHW Night Period Mon-Sat 10pm-7am Sun 10pm-8am	Any	CO1, CO2, RO	CO1, CO2, RO, AltA

Additional Mitigation Measures	
Measure	**Abbreviation**
Communication (Category 1)[1]	CO1
Communication (Category 2)[2]	CO2
Respite Offer[3]	RO
Alternative Accommodation	AltA
Agreement with Owners	AO

Note 1: CO1: Communication to provide information on the OOHW via methods such as letter box drop, email, newsletter, media advertisements and/ or website prior to the works commencing.

Note 2: CO2: Communication should be personalised (e.g. door knock, meeting, telephone call). Contact with these residents should commence early to enable feedback to be considered by the proposal.

Note 3: RO are not applicable to non-residential receivers. RO may comprise of pre-purchased movie tickets, dinner vouchers or similar. RO can also be provided by limiting high noise generating works and allowing at least a one-hour respite period between blocks of work. Where possible, the timing of this respite should be discussed with the impacted community.

Receiver Types			
Code	**Description**	**Code**	**Description**
RES	Residential	OED	Other Educational
COM	Commercial	OHO	Other Hotel
IND	Industrial	OLI	Other Library
OOA	Other Outdoor Active Recreation	OME	Other Medical
OOP	Other Outdoor Passive Recreation	OPW	Other Place of Worship
OCC	Other Child Care	OPB	Other Public Building



MARTINUS

Head Office | 3B, 33-35 Belmont Street / SUTHERLAND NSW 2232
